











Project Update Triskett Garage CNG Infrastructure Upgrades

Operational Planning & Infrastructure Committee July 13, 2021

Triskett Garage CNG Infrastructure Upgrade Project History

- Contract for \$6,262,600 awarded to Ruhlin Construction on December 15, 2020.
- Notice to Proceed was issued February 24, 2021.
- Project Kick-off March 23, 2021.
- Construction started April 5, 2021.
- Currently 30% complete.



- Steel reinforcement of selected columns and trusses has been completed as far as practical.
- Removed and replaced existing PVC sanitary sewer piping with cast iron.
- Ductwork replacement is 80% complete.
- Hose Reels are currently being installed.



Triskett Garage CNG Infrastructure Upgrade Due in July-

- Complete ductwork replacement / modification.
- Install firestopping insulation at the top of walls.
- Completion of hose reel installations.
- Commence & complete exhaust fan replacement.



• Base Contract: \$6,262,000

Change Orders to Date: \$10,030

Pending Change Orders: \$161,786

Projected Total: \$6,433,816

Invoiced to Date: \$887,722



Triskett Garage Project Schedule

Milestones	July	Aug	Sept	Oct	Nov	Dec	
Steel Reinforcement							
Sanitary Drain Replacement							
Ductwork							
Hose Reel Replacement							
Firestopping							
Overhead Doors							
Rooftop Equipment Replacement							
Painting							
Gas Detection System							
Building Automation System							
Generator Installation							
Substantial Completion							

Greater Cleveland Regional Transit Authority






New Ductwork



New Hose Reel

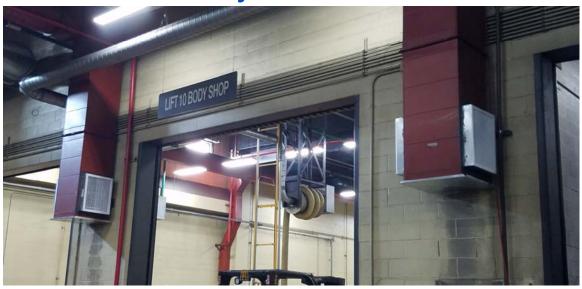

Modified Air Distribution



Modified Air Distribution

RIA



Modified Air Distribution



Modified Air Distribution



Modified Air Distribution

Questions?

